

2025 MAINTENANCE

Northwest Pipeline

March 2025

NYSE: WMB | www.williams.com



WE MAKE CLEAN ENERGY HAPPEN® **Williams**

AGENDA


Review 2025 Maintenance Items

- Meet the Team
- ILI Tool Runs
- Anomaly Work
- Pipeline Work
- Compressor Work
- Work with Impacts

Impact Mitigation Strategies

* ALL ITEMS LISTED IN THIS POWER POINT ARE SUBJECT TO CHANGE, REFER TO EBB FOR MOST UP TO DATE INFORMATION.

NORTHWEST PIPELINE CONTROL TEAM

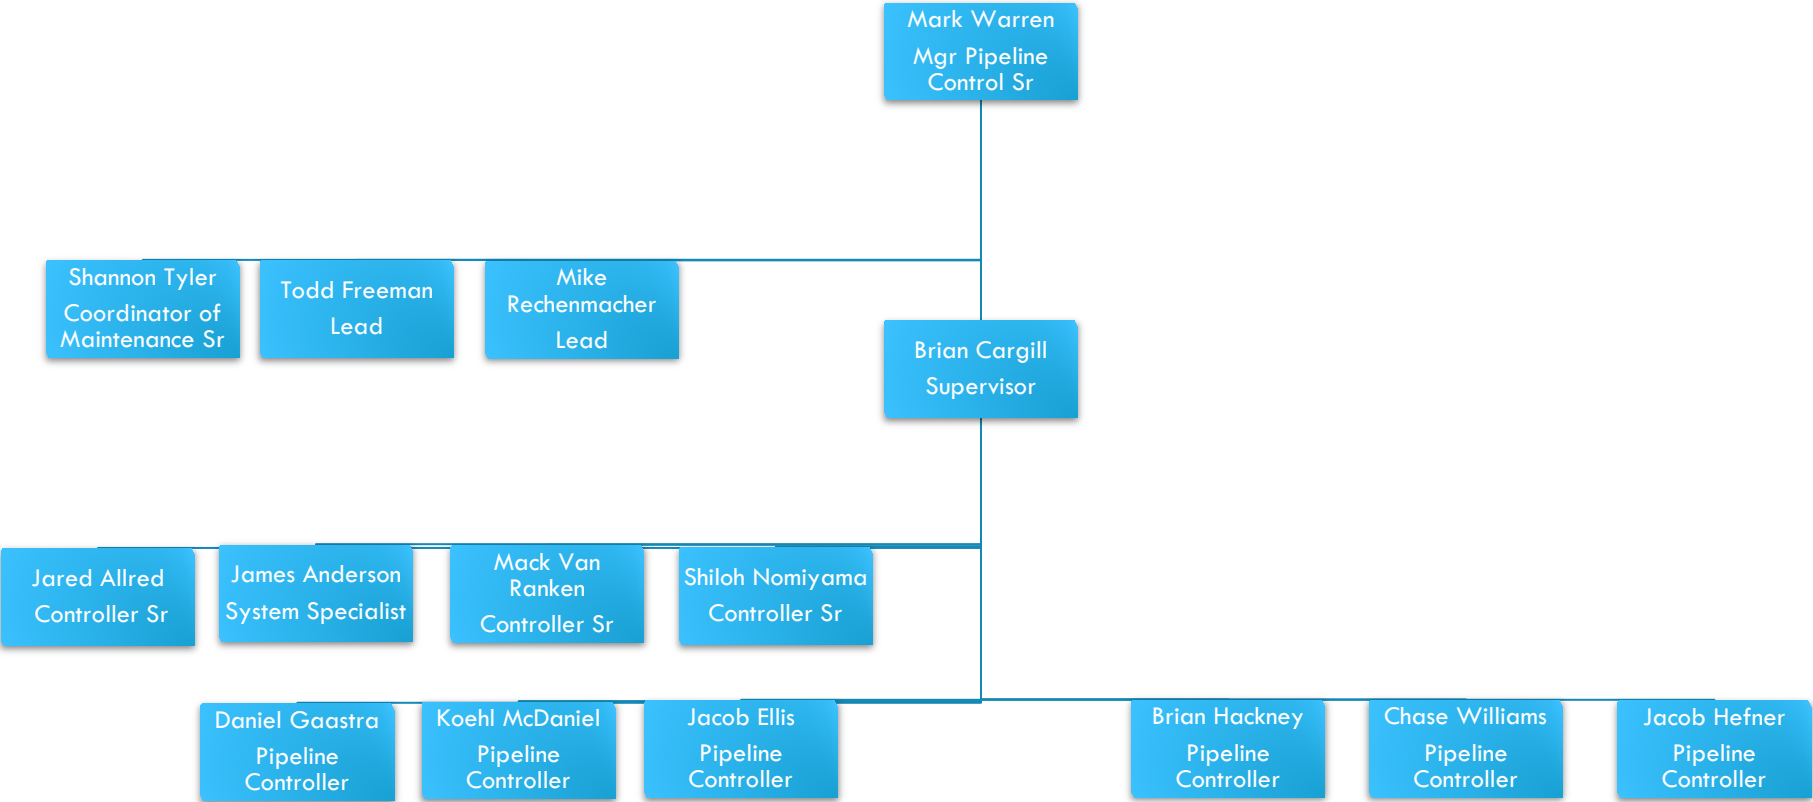


2025 MAINTENANCE PROJECTS: ILI TOOL RUNS




Point	Task Description	District	Start Date	End Date	Duration	Potential	Anticipated Impacts
1	Pocatello C/S to Burley C/s	Pocatello	4/15/2025	4/17/2025	2	Yes	No
2	Buhl C/S to Caldwell C/S	Pocatello/Boise	5/6/2025	5/8/2025	2	Yes	No
3	Baker C/S to Stanfield M/S	Boise	5/20/2025	5/24/2025	5	Yes	No
4	Plymouth C/S to Meacham C/S	Pasco	4/22/2025	5/1/2025		Yes	No
5	Plymouth C/S to Zillah C/S	Pasco	6/10/2025	6/19/2025		Yes	No
6	Coeur D'Alene Lat/Kellogg Lat	Spokane	4/15/2025	4/16/2025	2	Yes	No
7	Washougal C/S to SE Portland M/S	Eugene	6/10/2025	6/11/2025	2	Yes	No
8	Albany C/S to McKenzie River Span	Eugene	5/13/2025	5/17/2025	5	Yes	No
9	Centralia Lateral	Battleground	5/14/2025	5/15/2025	2	Yes	No
10	Chehalis C/S to Sumner C/S	Battleground	7/22/2025	7/23/2025	2	Yes	No
11	Sumner To Snohomish	Redmond	5/20/2025	5/21/2025	2	Yes	No
12	Evergreen Sedro Wooley Loop	Sumas	7/8/2025	7/10/2025	3	Yes	No

2025 MAINTENANCE PROJECTS: ANOMALY DIGS

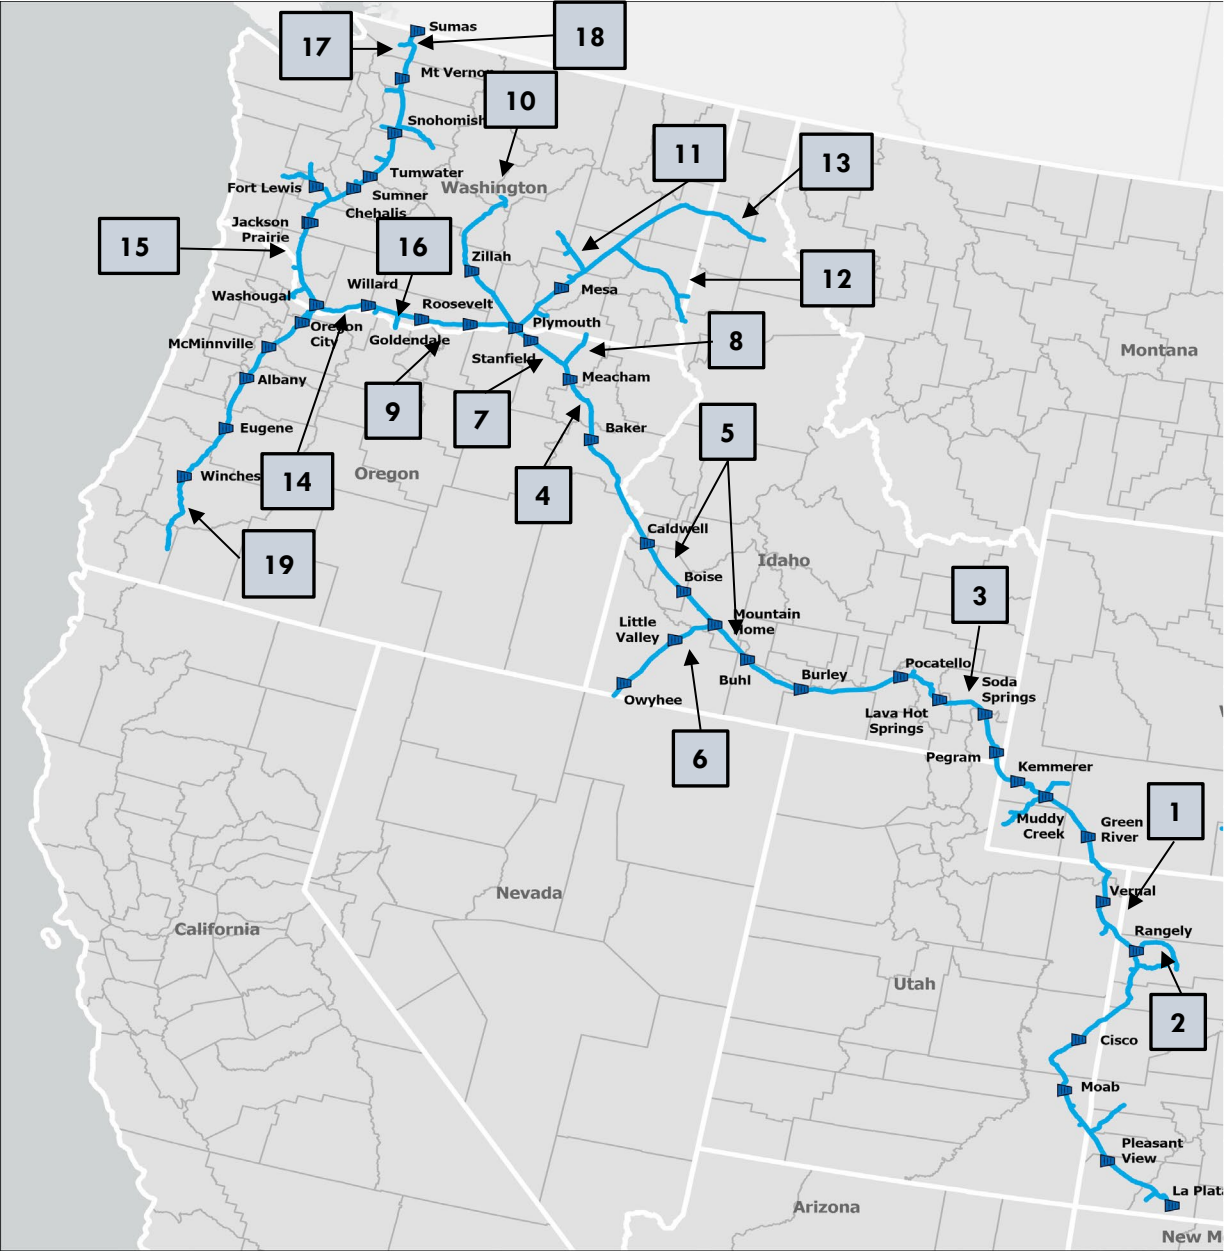

Point	Task Description	District	Start Date	End Date	Duration	Potential	Anticipated Impacts
1	Rangley to Vernal	Vernal	June	July		Yes	No
2	Piceance Lat	Vernal	Aug	Aug		Yes	No
3	Soda to Lava	Pocatello	5/28/25	7/3/25	37	Yes	No
4	Baker to Meacham	Boise	5/5/25	8/9/25	97	Yes	No
5	Snow River to Snow River	Boise	8/18/25	10/3/25	47	Yes	No
6	Reno Lateral	Boise	7/14/25	8/29/25	47	Yes	No
7	Meacham to Plymouth	Pasco	July	Aug		Yes	No
8	Walla Walla Lateral	Pasco	TBD	TBD		Yes	No
9	Roosevelt To Goldendale	Pasco	TBD	TBD		Yes	No
10	Alcoa Wenatchee to EOL	Pasco	TBD	TBD		Yes	No
11	Moses Lake Lateral	Spokane	June	June		Yes	No
12	Lewiston Lateral	Spokane	4/29/25	5/24/25	26	Yes	No
13	Coeur D'Alene Line/ Kellogg	Spokane	8/5/25	8/18/25	14	Yes	No
14	Willard to Washougal	Battleground	6/15/25	7/30/25	46	Yes	No
15	Washougal to Chehalis	Battleground	8/1/25	9/10/25	41	Yes	No
16	Dalles Lateral	Battleground	TBD	TBD		Yes	No
17	North Seattle Loop 16"	Redmond	8/1/25	8/30/25	30	Yes	No
18	North Seattle 8"	Redmond	6/1/25	6/15/25	15	Yes	No
19	Winchester to Grants Pass	Eugene	5/1/25	7/31/25	92	Yes	No

2025 MAINTENANCE PROJECTS: PIPELINE WORK

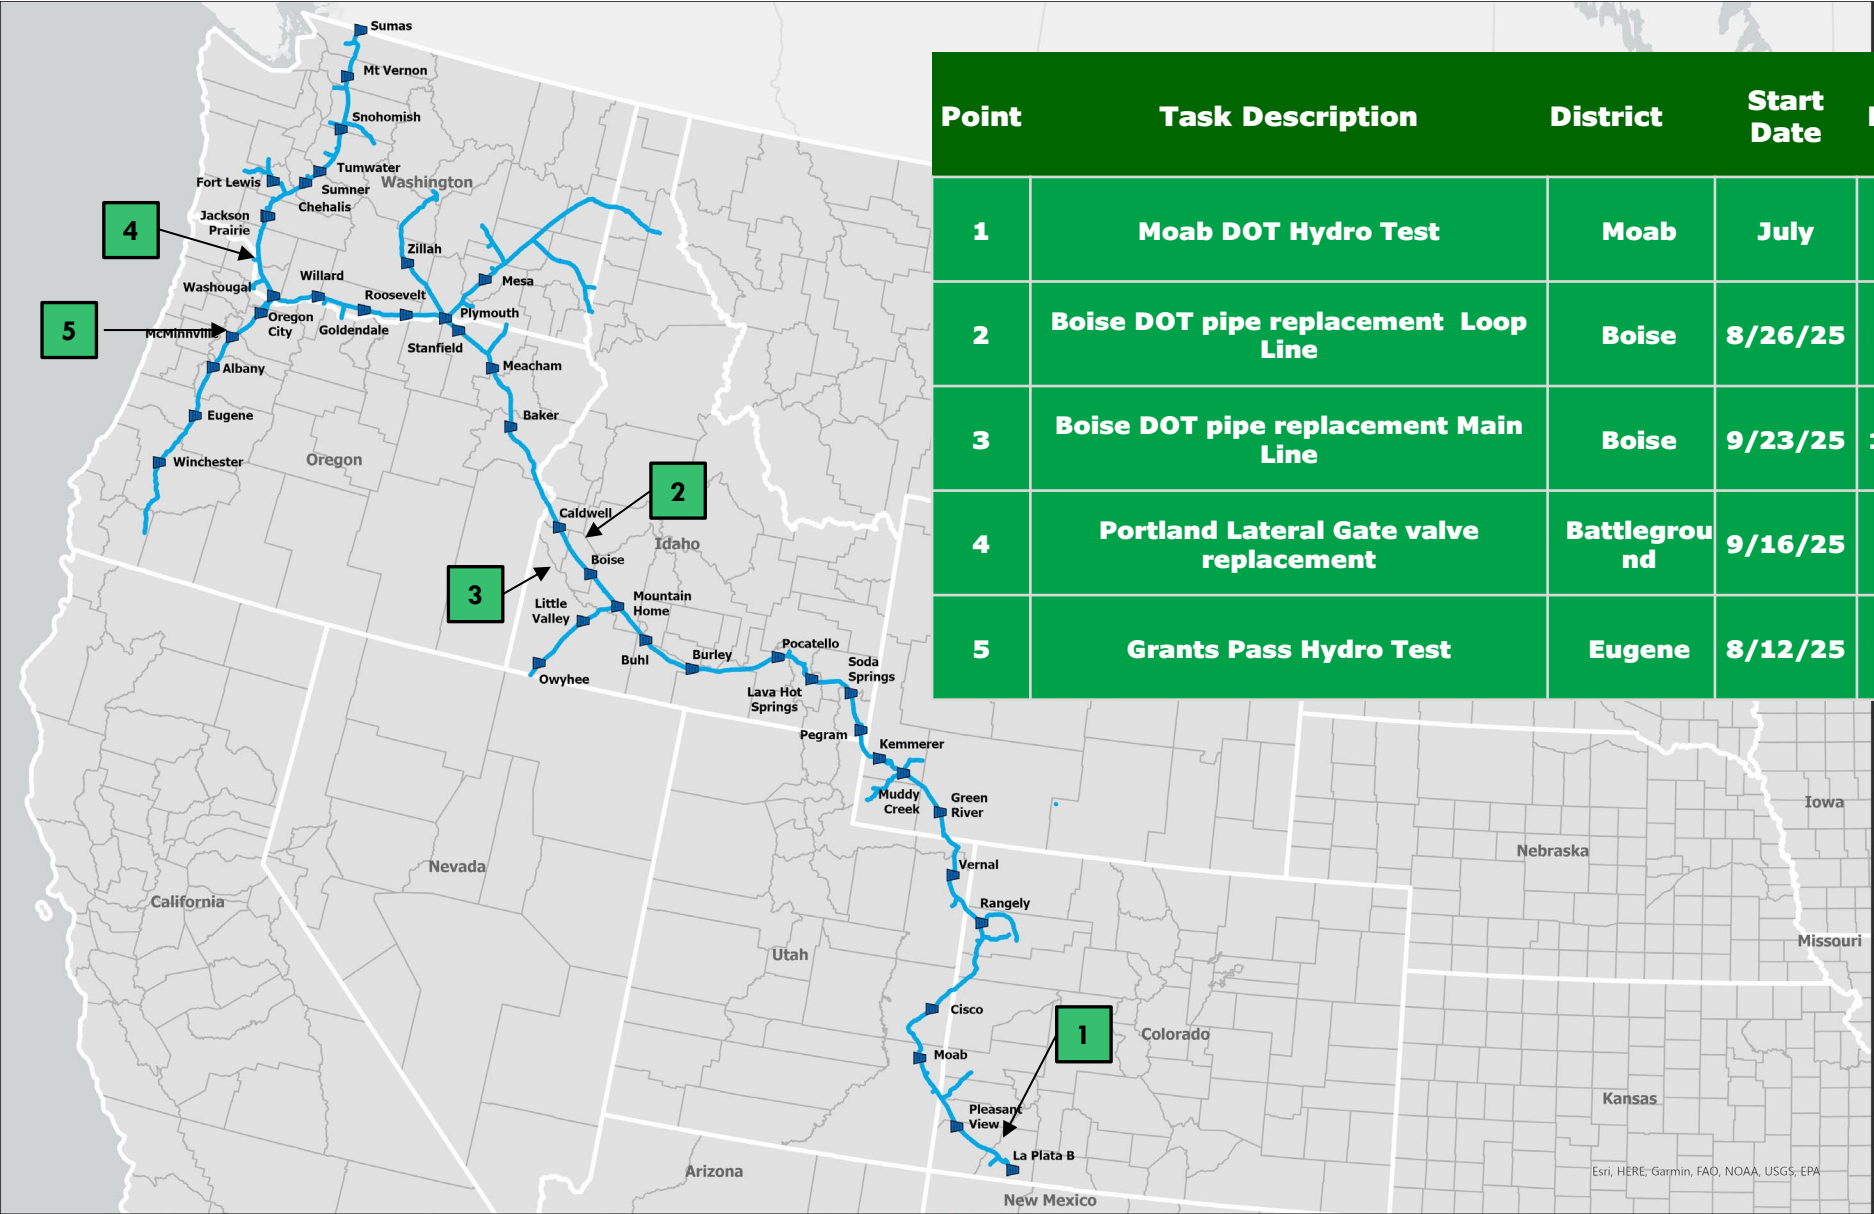


Point	Task Description	District	Start Date	End Date	Duration	Potential	Anticipated Impacts
1	Moab DOT Hydro Test	Moab	July	July	12	Yes	Yes
2	Boise DOT pipe replacement Loop Line	Boise	8/26/25	9/15/25	21	Yes	Yes
3	Boise DOT pipe replacement Main Line	Boise	9/23/25	10/27/25	35	Yes	Yes
4	Portland Lateral Gate valve replacement	Battleground	9/16/25	9/18/25	3	Yes	No
5	Grants Pass Hydro Test	Eugene	8/12/25	9/15/25	35	Yes	No

2025 MAINTENANCE PROJECTS: COMPRESSOR WORK AND M&ERP



Point	Task Description	District	Start Date	End Date	Duration	Potential	Anticipated Impacts
1	Cisco C/S M&ERP	Vernal	6/17/2025	10/31/2025	137	Yes	Yes
2	Muddy Creek M&ERP	Kemmerer	7/8/2025	10/15/2025	100	Yes	Yes
3	Pegram #2 M&ERP	Pocatello	7/24/2025	10/8/2025	77	Yes	Yes
4	Soda C/S M&ERP	Pocatello	8/1/2025	9/15/2025	46	Yes	Yes
5	Burley C/S inlet Filter Sperator	Pocatello	9/2/2025	9/23/2025	22	Yes	No
6	Buhl C/S Blow Down Silencer	Pocatello	5/13/2025	5/23/2025	11	Yes	No
7	Boise C/S Generator Replacement	Boise	4/15/2025	4/28/2025	14	Yes	No
8	Owyhee C/S Fuel Gas Reg	Boise	June	June		Yes	No
9	Zillah C/S Generator Replacement	Pasco	9/2/2025	9/22/2025	21	Yes	No
10	Snohomish #1 Eng Exchange	Redmond	6/23/2025	6/27/2025	5	Yes	No
11	Sumas A&B Plant disconnect	Sumas	4/14/2025	4/18/2025	5	Yes	YES

2025 MAINTENANCE IMPACTS

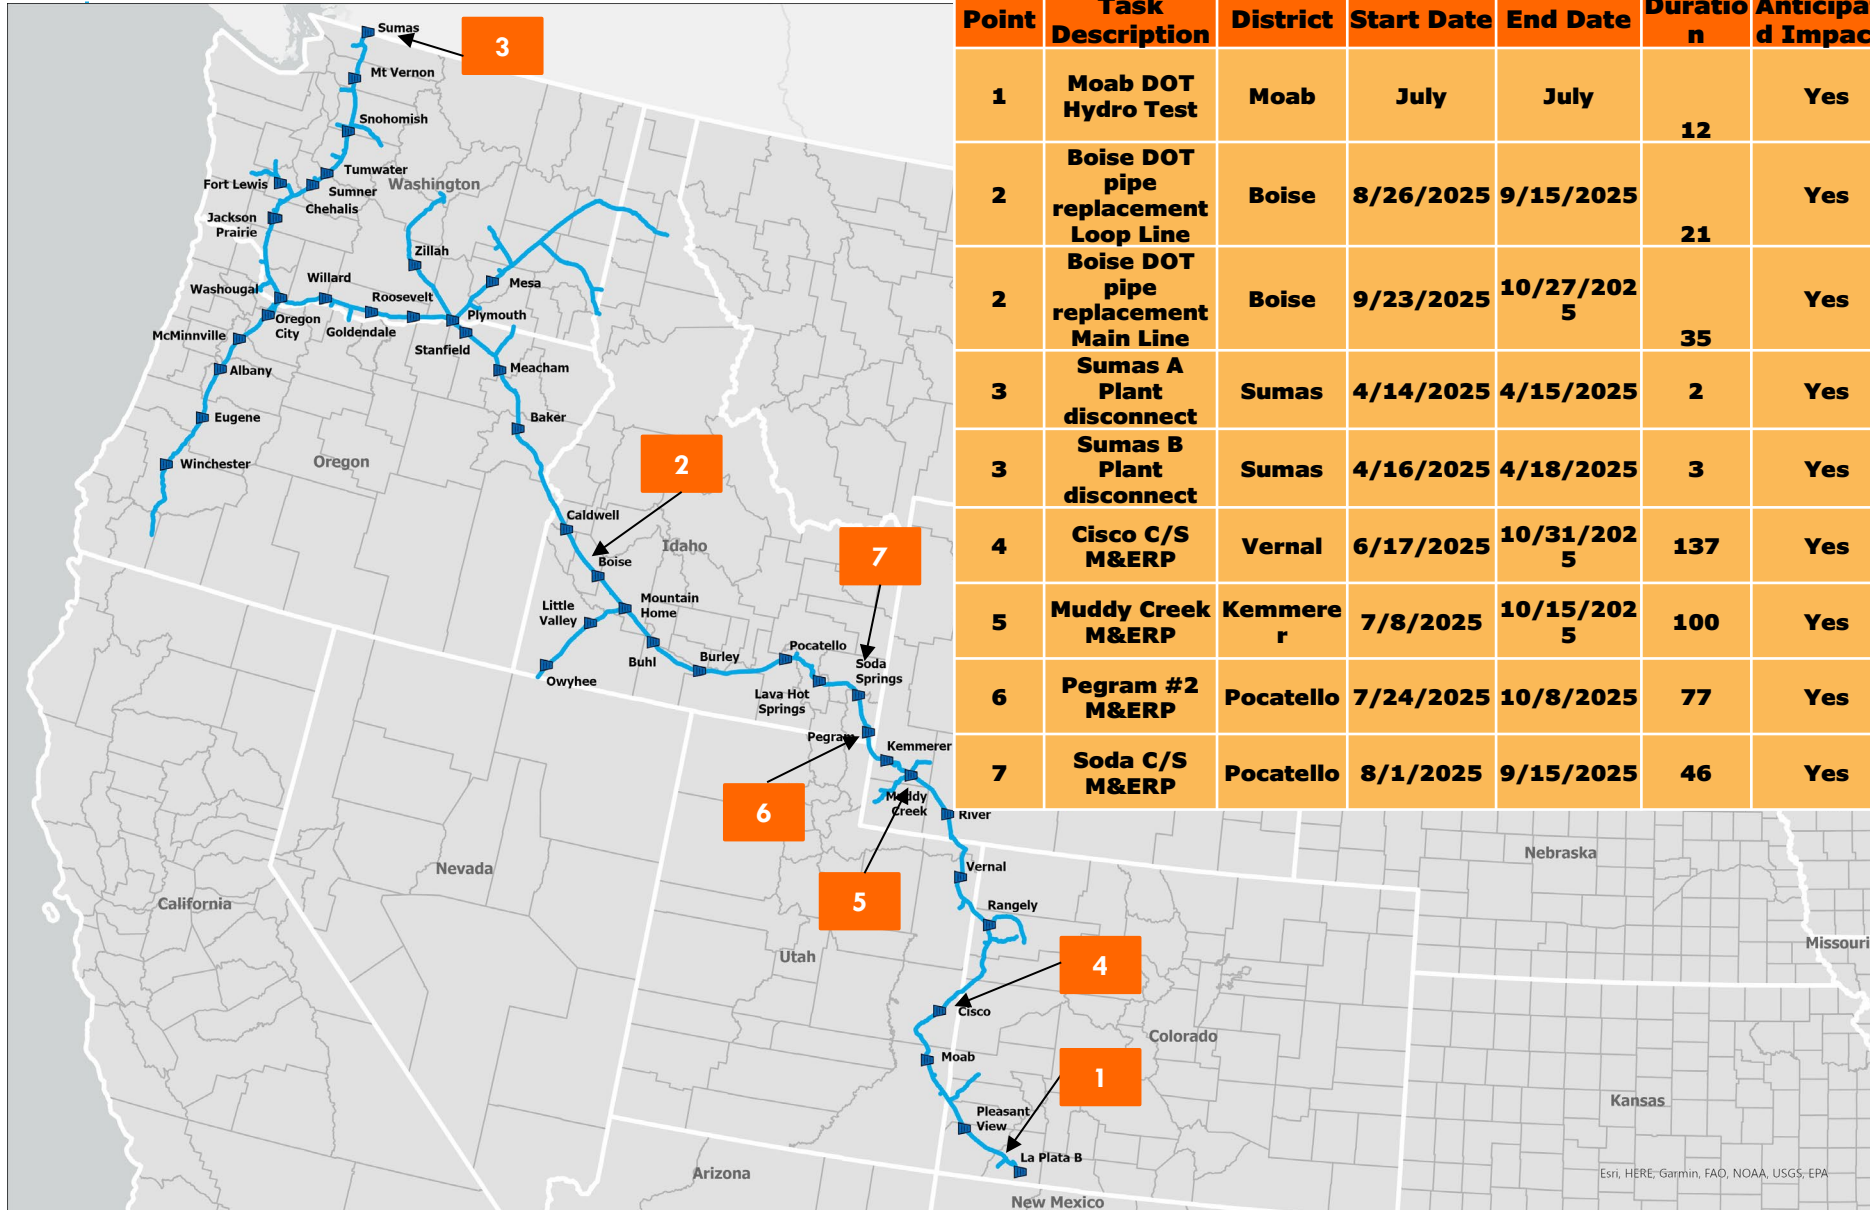

Point	Task Description	District	Start Date	End Date	Duration	Anticipated Impacts	Design Flow	Outage Flow	Flow Impact
1	Moab DOT Hydro Test	Moab	July	July	12	Yes	348 Dth S 278 Dth N	0	348 Dth S 278 Dth N
2	Boise DOT pipe replacement Loop Line	Boise	8/26/2025	9/15/2025	21	Yes	450 Dth N 452 Dth S	289 Dth N 286 Dth S	161 Dth N 166 Dth S
2	Boise DOT pipe replacement Main Line	Boise	9/23/2025	10/27/2025	35	Yes	450 Dth N 452 Dth S	373 Dth N 358 Dth S	77 Dth N 94 Dth S
3	Sumas A Plant disconnect	Sumas	4/14/2025	4/15/2025	2	Yes	1296 Dth	957 Dth	357 Dth
3	Sumas B Plant disconnect	Sumas	4/16/2025	4/18/2025	3	Yes	1296 Dth	810 Dth	504 Dth
4	Cisco C/S M&ERP	Vernal	6/17/2025	10/31/2025	137	Yes	286 Dth N 358 Dth S	241 Dth N 283 Dth S	45 Dth N 75 Dth S
5	Muddy Creek M&ERP	Kemmerer	7/8/2025	10/15/2025	100	Yes	654 Dth N	599 Dth N	55 Dth N
6	Pegram #2 M&ERP	Pocatello	7/24/2025	10/8/2025	77	Yes	653 Dth N	518 Dth N	135 Dth N
7	Soda C/S M&ERP	Pocatello	8/1/2025	9/15/2025	46	Yes	TBD	TBD	TBD

IMPACT MITIGATION STRATEGIES

- ☐ Analyze flow patterns to determine least impactful maintenance timeframes
- ☐ Coordinating with power generators, LDCs, end users and interconnects
- ☐ Avoid impacts to trading blocks as much as possible
- ☐ Utilizing multiple contractors in the same corridor at the same time
- ☐ Maximizing storage, line pack and interconnect flexibility
- ☐ Capitalizing on new and efficient technology
- ☐ Utilize stopple and bypass
- ☐ Plan inline inspections earlier in the year to avoid heating season impacts



CONCLUSION


Northwest will continue to provide updates.

Maintenance dates are subject to change.

The 2025 maintenance schedule is posted on Northwest's website at <http://www.northwest.williams.com>

Contact information:

- Mark Warren-Manager Pipeline Control Sr
Mark.P.Warren@williams.com
- Brian Cargill-Pipeline Control Supervisor
Brian.Cargill@williams.com
- Mike Rechenmacher- Pipeline Control Lead
Michael.Rechenmacher@williams.com
- Todd Freeman-Pipeline Control Lead
Todd.Freeman@williams.com
- Shannon Tyler-Pipeline Control Maintenance Coordinator Sr.
Shannon.Tyler@williams.com

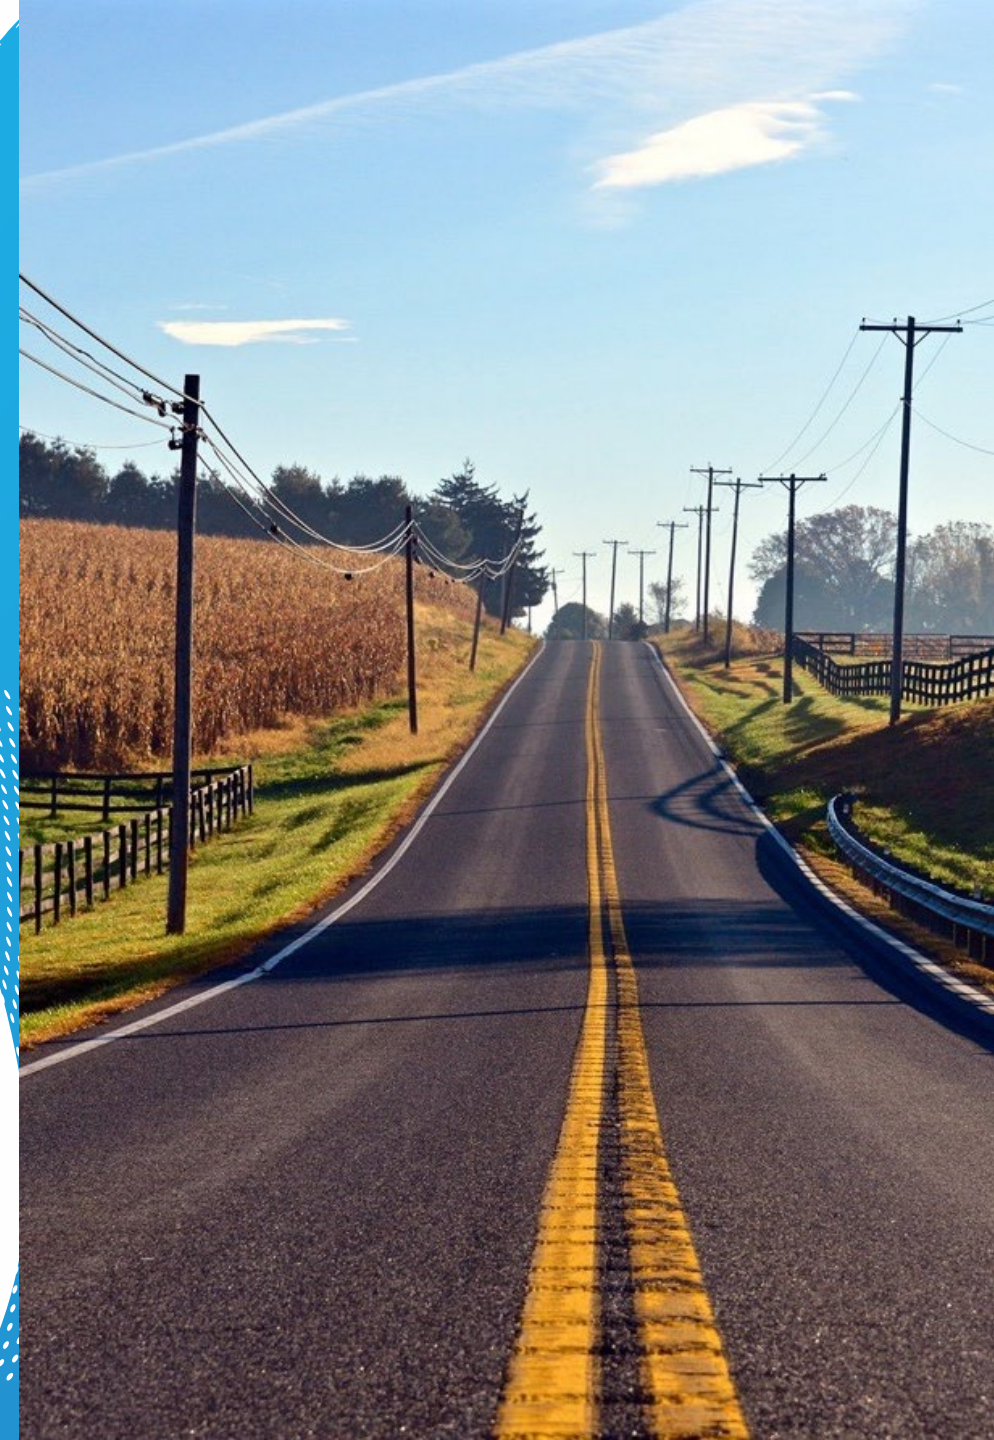



THANK YOU
